




Name of the work with location.	Construction of lane and drain near jk public school/Lawrence school at Panjterthi w.no.1.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.84
Project Initiation Year	2021
Date of Completion (MM/YY)	08.11.2021



Name of the work with location.	Constrction of lane / drain from h/o Mohan Lal to h/o Pushap Raj& Link h/o Sanjay allied works wno. 02.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.89
Project Initiation Year	2021
Date of Completion (MM/YY)	03.11.2021

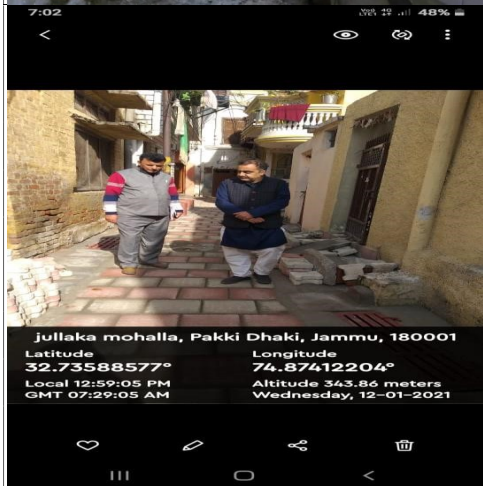

Name of the work with location.	Construction of defunct drain from h/o sh. Sanjay Kumar Towards Bitta Attachi Prem Nagar WNO. 07.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.92
Project Initiation Year	2021
Date of Completion (MM/YY)	28.01.2022




Name of the work with location.	Const. Drain from opp. Trikuta Complex to Gulshan Rahi 54/A Dogra Hall W No. 08.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.55
Project Initiation Year	2021
Date of Completion (MM/YY)	20.11.2021




Name of the work with location.	Ex. Hon'ble MLA and railing in steps and const. Of lane near h/o Anand house opp. Hanuman Mandir WNo. 09.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.70
Project Initiation Year	2021
Date of Completion (MM/YY)	19.03.2022



Name of the work with location.	Up gradation of lane from House of Parshotam Lal to Kali Dass..Kacha Talab Bahu Fort wno. 47.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.59
Project Initiation Year	2021
Date of Completion (MM/YY)	06.11.2021

	Name of the work with location.	Remodelling of lane and drain at Christian Colony, Bakshi Nagar Jammu Ward 27
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.64
	Date of start (MM/YY)	27.12.21
	Date of Completion (MM/YY)	31.12.21

	Name of the work with location.	Sr.No:20 Fixing Of Grating and Slab At Different Locations Of Ward No; 30 TalabTillo`
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.88
	Date of start (MM/YY)	29.11.21
	Date of Completion (MM/YY)	10.03.22




Sr. No.	33
Name of the work with Location	Repair / covering of drain from Hotel Gold Star to New Golden Hotel, Chand Nagar ward No. 19
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.82
Date of Start(Month/Year)	21-10-2021
Date of Completion (Month / Year)	27-11-2021
No. of beneficiaries	300



Sr. No.	34
Name of the work with Location	Upgradation of lane by way of tiles near H.No. 16 A/C H/o Janak Singh Ward No. 20
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.62
Date of Start(Month/Year)	07-09-2021
Date of Completion (Month / Year)	25-09-2021
No. of beneficiaries	150



Name of the work with Location	up gradation of lane/drain including steel gratings at spots in Cornol colony ward no 41
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.61
Date of Start(Month/Year)	05-10-2021
Date of Completion (Month / Year)	30-10-2021
No. of beneficiaries	250

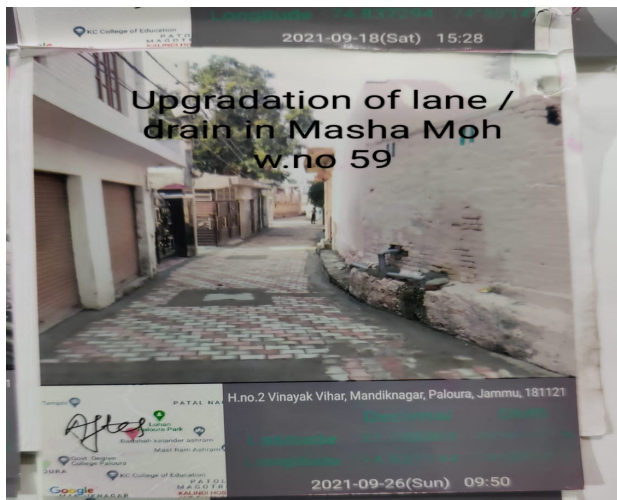

Name of the work with Location	up gradation of lane by w/o laying Paver tiles in Masha Mohalla ward no.59
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.52
Date of Start(Month/Year)	15-09-2021
Date of Completion (Month / Year)	30-09-2021
No. of beneficiaries	300

Upgradation of lane /
drain in Tammani Moh
nr Tiny Tots School
W.no 60



Jammu, null, null
Unnamed Road, Sector 1, Paloura,
Jammu, 181121
Lat 32.7627°
Long 74.831828°
08/10/21 08:49 AM


Sr. No.	37
Name of the work with Location	Up gradation of land and drain in Tammani Mohalla near pond Dhok Paloura W.No 60
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.70
Date of Start(Month/Year)	08-09-2021
Date of Completion (Month / Year)	30-09-2021
No. of beneficiaries	200

**up gradation of lane
near park in w no 61**



Sr. No.	38
Name of the work with Location	Upgradation of lane at ManormaVihar near Park in ward No. 61
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.60
Date of Start(Month/Year)	30-08-2021
Date of Completion (Month / Year)	28-09-2021
No. of beneficiaries	300


**up grad lane laxmipuram
chinoor in w no 62**

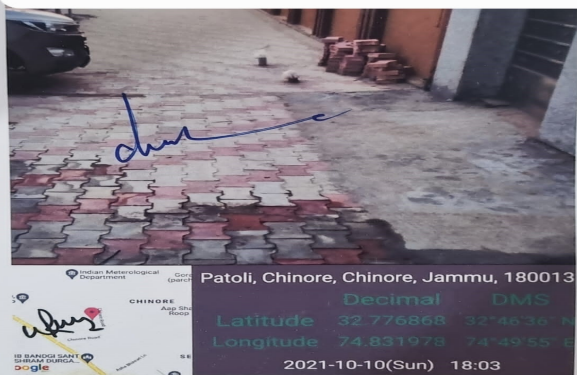


Sr. No.	39
Name of the work with Location	Construction / up gradation of lane by way of laying of paver tiles at Laxmipuram near Maqbool Choudhary in ward No. 62
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.51
Date of Start(Month/Year)	30-08-2021
Date of Completion (Month / Year)	28-09-2021
No. of beneficiaries	100

	Sr. No.	40
	Name of the work with Location	Construction / up gradation of lane at Bharat nagar in ward No. 63
	Department/Organisation	H&UDD
	Executive Agency	JAMMU MUNICIPAL CORPORATION
	Block/District	JAMMU
	AA Cost (Rs . in Lakhs)	2.65
	Total Cost of Completion/expenditure incurred ending 3/2022	1.51
	Date of Start(Month/Year)	30-08-2021
	Date of Completion (Month / Year)	28-09-2021
	No. of beneficiaries	100

	Sr. No.	41
	Name of the work with Location	Upgradation of lane / drain near H/o AmanSansyal near Hanjura lane in ward no. 64
	Department/Organisation	H&UDD
	Executive Agency	JAMMU MUNICIPAL CORPORATION
	Block/District	JAMMU
	AA Cost (Rs . in Lakhs)	2.65
	Total Cost of Completion/expenditure incurred ending 3/2022	1.51
	Date of Start(Month/Year)	30-08-2021
	Date of Completion (Month / Year)	28-09-2021
	No. of beneficiaries	140

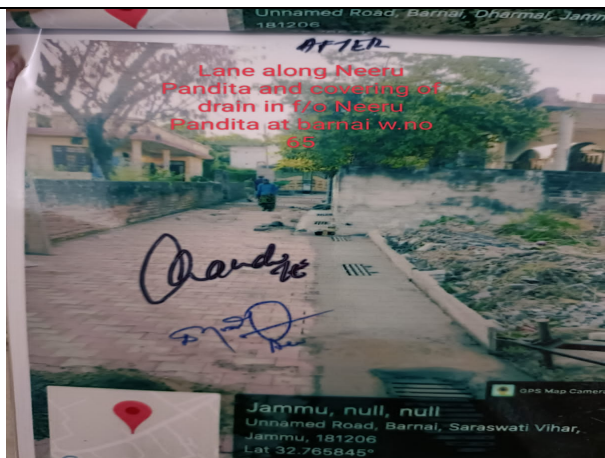

Sr. No.	42
Name of the work with Location	Up gradation of lane along H/o NeeruPandita and covering of drain in front of NeeruPandita at Barnai in ward No. 65
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.64
Date of Start(Month/Year)	16-09-2021
Date of Completion (Month / Year)	05-10-2021
No. of beneficiaries	160

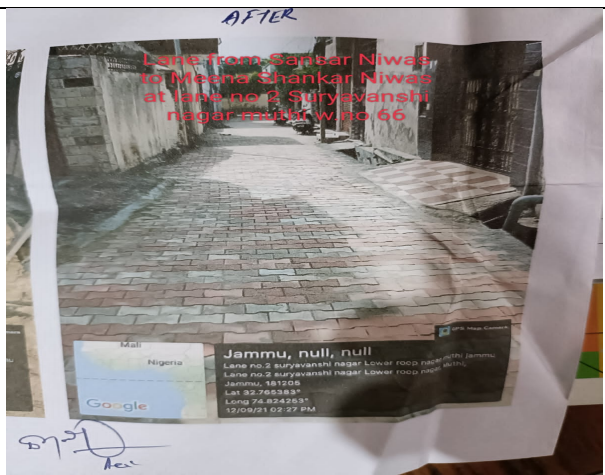

Sr. No.	43
Name of the work with Location	Up gradation of lane from H/o Sansar Niwas at MeenaShanker Niwas at lane No. 2 Suryavanshi Nagar Muthi ward no. 66
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.55
Date of Start(Month/Year)	26-08-2021
Date of Completion (Month / Year)	15-09-2021
No. of beneficiaries	150



Sr. No.	44
Name of the work with Location	Up gradation of lane along H/o Bobby Dutta at amit Nagar Muthi in ward No. 67
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.51
Date of Start(Month/Year)	29-08-2021
Date of Completion (Month / Year)	22-10-2021
No. of beneficiaries	160




Sr.no	8
Name of the work with Location	Upgradation of lane drain by way of the precast interlocked tiles from H/o.Handoo Niwas h.no 286 to onwards and allied works near h.no265 in ward no43 under CCDP Head 21-22
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.69
Date of Start Month/Year	8-8-2021
Date of Completion	22-8-2021
No of Beneficiaries	390



Sr.no	9
Name of the work with Location	Covering of drain with grating and RCC Slabs form the H/o. Harjinder singh Hno.40 to Hno.45 at lane no.10 sec-7 Nanak Nagar Jammu ward no. 44
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.90
Date of Start Month/Year	10-9-2021
Date of Completion	8-10-2021
No of Beneficiaries	520



Sr.no	10
Name of the work with Location	Upgradation of lane by way of precast interlock tiles near culvert from H/o. of P.C.Dayal Hno. 150 to onwards in ward no. 45 Preet Nagar under CCDP Head for the year 21-22
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.52
Date of Start Month/Year	15-8-2021
Date of Completion	12-9-2021
No of Beneficiaries	470

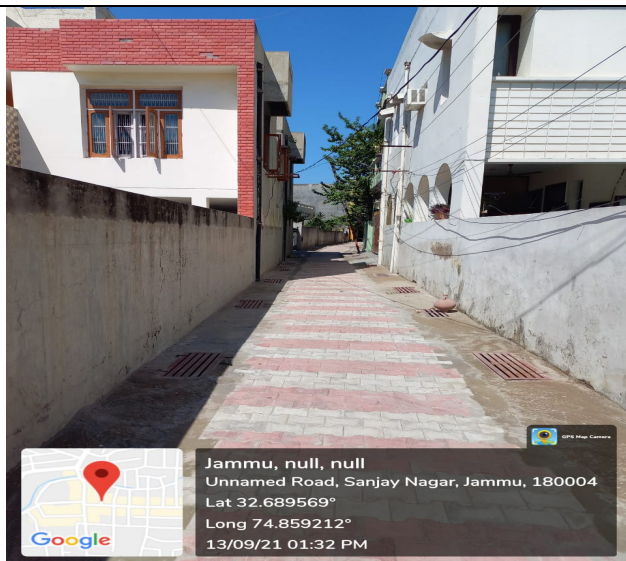

Sr.no	11
Name of the work with Location	Upgradation /repair of lane in H/o. Attar Singh Vali lane & its adjoining lane sec-2 Sanjay Nagar ward no.46
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.57
Date of Start Month/Year	12-8-2021
Date of Completion	11-9-2021
No of Beneficiaries	250



Sr.no	12
Name of the work with Location	Constt./ Upgradation of lane from H/o. Chowdhary to H/o. Anoop Malhotra at South Extn. Trikuta Nagar ward no.52
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.56
Date of Start Month/Year	15-8-2021
Date of Completion	1-9-2022



Sr.no	13
Name of the work with Location	Construction of the tile work in lane from Hno.63P, II extrn. Khoo wali Gali Vijay Sharma in ward no.53
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.55
Date of Start Month/Year	1-3-2022
Date of Completion	17-3-2022
No of Beneficiaries	500



Sr.no	14
Name of the work with Location	Upgradation of rain from H/o.41,42,43,44-P Sec-6 and near SBI Bank sector-5A , Trikuta Nagar ward no.54
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.62
Date of Start Month/Year	9-8-2021
Date of Completion	7-9-2021
No of Beneficiaries	160



Sr.no	15
Name of the work with Location	Upgradation of lane providing & fixing of interlock tiles in kashmiri Mohalla (Pandit) Gangyal at ward no.56
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.58
Date of Start Month/Year	16-10-2021
Date of Completion	29-10-2021
No of Beneficiaries	190



Sr.no	16
Name of the work with Location	Providing and fixing of the interlock tiles in Mohalla Roop-Nagar Gangyal ward no.57 under CCDP Head for the year 21-22
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.72
Date of Start Month/Year	15-10-2021
Date of Completion	15-11-2021
No of Beneficiaries	222



Sr.no	18
Name of the work with Location	Construction of lane by way of interlocked tiles from H/o. Sukhvinder Singh to H/o. L.S.Sokhia Singh links lane no.10 ,98 at ward no.68
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.52
Date of Start Month/Year	21-9-2021
Date of Completion	16-3-2022
No of Beneficiaries	250



Sr.no	19
Name of the work with Location	Construction of the drain near Stadium sector-G in ward no.69 Sainik Colony under CCDP Head for the year 21-22.
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.57
Date of Start Month/Year	16-10-2021
Date of Completion	12-11-2021
No of Beneficiaries	350



Sr.no	20
Name of the work with Location	Construction of drain at sector –D from Hno.78 Sainik Colony ward no.70 (near little flower school)
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.56
Date of Start Month/Year	7-12-2021
Date of Completion	5-3-2022
No of Beneficiaries	450



Sr.no	21
Name of the work with Location	Construction/ Upgradation of drain near Gurudwara lower Gadigarh ward no.73
Department/Organization	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.80
Date of Start Month/Year	3-9-2021
Date of Completion	22-10-2021



Sr. No.	1
Name of the work with Location	Upgradation of Lane Drain in Dogra Mohalla Krishna Nagar Ward. No. 12
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.88
Date of Start (Month/Year)	09-08-2021
Date of Completion(Month/Year)	15-09-2021
No. of beneficiaries	



Sr. No.	2
Name of the work with Location	Upgradation of Lane and Drain from H/O Mohan Lal to H/O Ashok Kumar Resham Ghar Colony ward No. 13
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.97
Date of Start (Month/Year)	09-08-2021
Date of Completion(Month/Year)	01-09-2021
No. of beneficiaries	



Sr. No.	3
Name of the work with Location	Construction of Lane and Drain from H/O Anil Gupta to H/O Rakesh Gupta in Sector-3 Bhagwati Nagar Ward No. 14
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.99
Date of Start (Month/Year)	09-08-2021
Date of Completion(Month/Year)	30-08-2021
No. of beneficiaries	




Sr. No.	4
Name of the work with Location	Construction of Lane and Drain from House of R. P Sharma to House of Katoch Ward No. 16
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.48
Date of Start (Month/Year)	12-11-2021
Date of Completion(Month/Year)	09-02-2021
No. of beneficiaries	




Sr. No.	5
Name of the work with Location	Upgradation of Lane by way of tiling from House of Ram Murti to House of Mohinder Pal including side lane.
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.52
Date of Start (Month/Year)	18-10-2021
Date of Completion(Month/Year)	22-12-21



Sr. No.	6
Name of the work with Location	Construction/Up-gradation of Drain and Slab on road along H. No. 53, 54, 64 in Ward No. 22
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.96
Date of Start (Month/Year)	23-08-2021
Date of Completion(Month/Year)	22-09-2021
No. of beneficiaries	300

	Sr. No.	7
	Name of the work with Location	Upgradation of Lane from Sham Tailor Shop to H. No. 121 by way of P/L Tiles Ward No. 23
	Department/Organization	H&UDD
	Executing Agency	JAMMU MUNICIPAL CORPORATION
	Block/District	Jammu
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.87
	Date of Start (Month/Year)	10-08-2021
	Date of Completion(Month/Year)	20-02-2022
	No. of beneficiaries	250

	Sr. No.	8
	Name of the work with Location	Upgradation of Lane and Drain from H. No. 41 to 45 near Heritage Apartment and from H/O Surjeet Gupta to H/O Shanti Ward No. 24
	Department/Organization	H&UDD
	Executing Agency	JAMMU MUNICIPAL CORPORATION
	Block/District	Jammu
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.62
	Date of Start (Month/Year)	31-08-2021
	Date of Completion(Month/Year)	01-10-2021



Sr. No.	9
Name of the work with Location	Upgradation of lane and drain from House of Manu Jamwal
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.10
Date of Start (Month/Year)	06-12-21
Date of Completion(Month/Year)	23-12-21



Sr. No.	10
Name of the work with Location	Construction of Lane from H/o Balbir Upto H/o Satpal and H/o Ashwani Kumar upto H/o Ratan Lal by way of P/L Interlocking Tiles Ward No. 48
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.60
Date of Start (Month/Year)	20-12-2021
Date of Completion(Month/Year)	03-01-2022



Sr. No.	11
Name of the work with Location	Construction of Lane in Guru Ravi Dass Mohalla Upper Ward No. 49
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.68
Date of Start (Month/Year)	03-08-2021
Date of Completion(Month/Year)	12-12-2021



Sr. No.	12
Name of the work with Location	Upgradation of Lane and Drain in Sector-1 along the park Ward No. 50
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.53
Date of Start (Month/Year)	16-08-2021
Date of Completion(Month/Year)	12-09-2021



Sr. No.	13
Name of the work with Location	Construction of lane near Saudh Mohalla / Brahman Mohalla by way of tilling.
Department/Organization	H&UDD
Executing Agency	JAMMU MUNICIPAL CORPORATION
Block/District	
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.38
Date of Start (Month/Year)	2-09-2021
Date of Completion(Month/Year)	30-09-2021
