

Name of the work with location.	Black topping of lanes back side of Arya SamajMandir and along AaryaSamaj Park in Ward No: 28 Bakshi Nagar Jammu
Department/Organization	H&UDD
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	5.35
Total Expdtd incurred ending 3/2022	5.31
Date of start (MM/YY)	18.02.22
Date of Completion (MM/YY)	08.03.22



Name of the work with location.	premixing of lane No: 17 (Guru Ravi Das ji Temple) and lane No: 29, Rajpura
Department/Organization	H&UDD
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	7.10
Total Expdtd incurred ending 3/2022	5.24
Date of start (MM/YY)	10.11.21
Date of Completion (MM/YY)	02.07.22



Name of the work with location.	Premixing of lane No: 1, 2, 8 and 9 of Shakti Nagar Ward No: 29
Department/Organization	H&UDD
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	11.44
Total Expdt incurred ending 3/2022	10.57
Date of start (MM/YY)	07.11.21
Date of Completion (MM/YY)	03.03.22



Name of the work with location.	Rep/Remodeling of lane from shop of KrishanPansariUpto H/o Ashok Kumar Anmol General Store Lane No: 10, from H/o BattanMaisi to H/o Manga Ram near Nallah and L.No: 4, Repair/Remodelling of lane from Subash Milk Shop to H/o Gurnam Singh, Repair/remodeling of lane from H/o Sansormistri to H/o Rajesh Gupta and lane from near transformer along R/s of Nalah Shakti Nagar, Upgradation/constt of lane from bbackside of AmbedkarChowk to Backside of Rajpura Park near transformer, Repair/remodeling of lane no: 8 opp. KrishanPansari Shop Rajpura from Chowk to Sat Ashram
Department/Organization	H&UDD
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	35.00
Total Expdt incurred ending 3/2022	21.46
Date of start (MM/YY)	08.02.22
Date of Completion (MM/YY)	20.03.22
No of beneficiaries	




Name of the work with location.

Upgd of L/D from H/o Ram Lal Saini /Ambe Transformer upto H/o Chajju Singh ShantNagar , Lane Opp. Swarna Niwas 3/115 Indira Viharupto H/No. 104 Ram vihar, lane from Doctor Clinic upto H/o KarilalooHNo. 2/106 Ram Vihar, L/D From Shop of Sham PansariuptoSubashChanderShant nagar, From H/o Sh. Ram das upto Om Parkash ,From H/o Sh. Sukesh Thakur HNo. 176/B upto H/o Tara Chand HNo. 265-C ram Vihar ,Imp/ Ren. of L/D Khanna Lane Opp. Bread factory Pandoka Colony D/E for Upgd of lane by way of Paver tiles and Reconst. drains along the lane from the h/o RajnikoulHNo 62 upto h/oPuran Singh


Department/Organization	H&UDD
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	35.00
Total Expdt incurred ending 3/2022	20.73
Date of start (MM/YY)	30.01.22
Date of Completion (MM/YY)	22.03.22



Name of the work with location.	D/E for Upgradation of lane, From Vikas General Store to Luthra House and , Lane opp Mahajan Enterprises at Janipur ward No. 37, Lane from Raj kumarKhajuriaupto H/o Satish Sharma at Janipur colony Ward no. 3, lane back side H/o advocate Sh. Sandeep Gupta at Janipur Ward no. 37, Lane around Park Major Ajay Singh Jasrotia and veer Savar Bar Park ward No. 37, Lane from H/o DalipGambel to H/o Subhdev Raina near Shiv Mandir Janipur ward No. 37
Department/Organization	H&UDD
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	35.00
Total Expdt incurred ending 3/2022	20.90
Date of start (MM/YY)	18.01.22
Date of Completion (MM/YY)	24.02.22

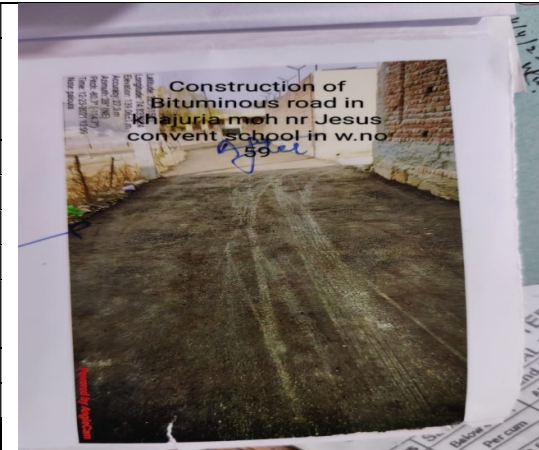

<b>Name of the work with Location</b>	<b>(i) Construction of Bituminous road in Khajuria Mohalla near Jesus Convent School &amp; Link Road W. NO. 59</b>
<b>Department/Organisation</b>	<b>H&amp;UDD</b>
<b>Executive Agency</b>	<b>JAMMU MUNICIPAL CORPORATION DIVISION NO. IIII</b>
<b>Block/District</b>	<b>JAMMU</b>
<b>AA Cost (Rs . in Lakhs )</b>	<b>9.71</b>
<b>Total Cost of Completion/expenditure incurred ending 3/2022</b>	<b>8.29</b>
<b>Date of Start(Month/Year)</b>	<b>01-12-2021</b>
<b>Date of Completion ( Month / Year)</b>	<b>22-12-2021</b>
<b>No. of beneficiaries</b>	<b>500</b>

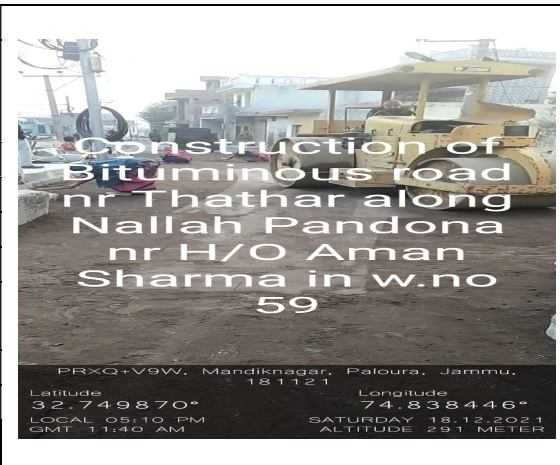

<b>Name of the work with Location</b>	<b>(ii) Construction / Upgradation of Bituminous road near Thathar along Nallah Pandona Near H/o Aman Sharma W.NO. 59</b>
<b>Department/Organisation</b>	<b>H&amp;UDD</b>
<b>Executive Agency</b>	<b>JAMMU MUNICIPAL CORPORATION DIVISION NO. III</b>
<b>Block/District</b>	<b>JAMMU</b>
<b>AA Cost (Rs . in Lakhs )</b>	<b>19.58</b>
<b>Total Cost of Completion/expenditure incurred ending 3/2022</b>	<b>18.98</b>
<b>Date of Start(Month/Year)</b>	<b>01-12-2021</b>
<b>Date of Completion ( Month / Year)</b>	<b>02-01-2022</b>
<b>No. of beneficiaries</b>	<b>700</b>

**up grad of road Jmc  
road in w no 63**



Name of the work with Location

Upgradation of lane b/w of laying premix carpet lane no. 6,5,4,1 near carpenter office kamal nagar Sector – II near Govt. School to H/o Banam Singh to Mh. Gulam in W.No. 63

Department/Organisation

H&UDD

Executive Agency

JAMMU MUNICIPAL CORPORATION DIVISION NO. III

Block/District

JAMMU

AA Cost (Rs . in Lakhs )

32.80

Total Cost of Completion/expenditure incurred ending 3/2022

31.15

Date of Start(Month/Year)

20-02-2022


Date of Completion ( Month / Year)

29-03-2022

No. of beneficiaries

850

**up grad of lane drain  
lower upper thather k v  
nagar bantalab in w no  
63**

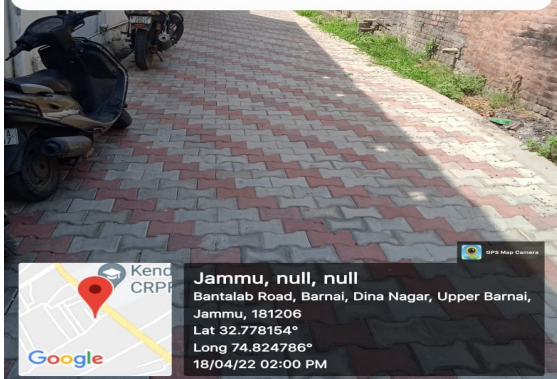

Name of the work with Location

Construction of Lane / Drain at near Peepal Tree / Near Puran Singh at Keran and Lane at Lower Thather Near H/o Puran Singh / H/o Jay Singh / H/o Ashok Kuyamar / H/o Harbans Lal and near Bharwali Chapri, Upgradation of lane at Bhagat Mohalla UpperThather and Lane Drain from H/o Subash Verma to Suraj Verma at Thather, Upgradation of lane at KV Nagar / Thather / Keran Bantalab W. NO. 63

Department/Organisation

H&UDD

Executive Agency

JAMMU MUNICIPAL CORPORATION DIVISION NO. III

Block/District

JAMMU

AA Cost (Rs . in Lakhs )

34.50

Total Cost of Completion/expenditure incurred ending 3/2022

18.87

Date of Start(Month/Year)

20-01-2022

Date of Completion ( Month / Year)

20-03-2022

**up grad of lane drain  
shazadpur ganguwan  
in w no 72**



Name of the work with Location

Const of lane from H/o Prem Singh to h/o Mangal Singh and allied links at Mohalla , L/D from H/o Parveen Singh to Main Road and drains from Shankar Singh to Mangal Singh at Gangwan Shehzadpur, Lane from Parveen Kumar House to Raj Kumar House and Ram Pal to Hans Raj house and drain from h/o Hem Raj to virshi house, Const of lane from Balwan Singh House to Main Road Shehzadpur and allied links to house of Amar Nath and Gattu Ram, L/D from H/o Sanga Ram to Main Road Patyalichak., L/D from H/o Mohan Lal to Tikri Road, L/D main road Darian to house of Des Raj PatyaliChak. W.NO. 72

Department/Organisation

H&UDD

Executive Agency

JAMMU MUNICIPAL CORPORATION DIVISION NO. III

Block/District

JAMMU

AA Cost (Rs . in Lakhs )

34.50

Total Cost of Completion/expenditure incurred ending 3/2022

25.60

Date of Start(Month/Year)

25-01-2022

Date of Completion ( Month / Year)

10-03-2022

No. of beneficiaries

600





Name of the work with Location	Macadamization of Road by w/o premixing at internal roads of sec-5 A Trikuta Palace sec-5,6,7,8 and 9 in Trikuta Nagar in ward no 54
Department/Organization	H&UDD
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	23.50
Total Cost of Completion/Expenditure Incurred ending 3/2022	18.23
Date of Start Month/Year	1-3-2022
Date of Completion	14-3-2022
No of Beneficiaries	385



Name of the work with Location	Macadamization of Roads by w/o premixing at Internal roads of Green Avenue Model Town, Akali kour Singh Jeevan Nagar Ward no 58
Department/Organization	H&UDD
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	33.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	30.75
Date of Start Month/Year	5-11-2021
Date of Completion	26-3-2022
No of Beneficiaries	300



Name of the work with Location	Constt. of lane and rain from shakti tent house to Sardari Lal h no 626 Digiana ward no 45, Repair/covering of drain at various locations in Digiana and preet nagar ward no 45, Constt. of lane no 1 from H/o Milki Ram to Janak sehni house digiana and vijay kumar to H/o Megh nath Gupta preet nagar near Ravi Dass temple ward no 45
Department/Organization	H&UDD
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	34.50
Total Cost of Completion/Expenditure Incurred ending 3/2022	20.83
Date of Start Month/Year	3-2-2022
Date of Completion	16-3-2022
No of Beneficiaries	700



Name of the work with Location	Upgradation of lane by way of paver tiles from H/o. Rugavir singh Jamwal to onwards in ward no.52, Upgradation of lane by way of paver tiles near Hno.303 sector Trikuta Nagar (South extn.)ixing of gratings & slabs near H/o. Jadjish kumar & Balvinder singh (South extn. ), Upgradation of lane by way of paver tiles near lane no.1/A opp. Tube well near Harvinder Public School., Upgradation of lane by paver tiles in east extn. Marble lane IV ward no.52
Department/Organization	H&UDD
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	34.50
Total Cost of Completion/Expenditure Incurred ending 3/2022	15.13
Date of Start Month/Year	12-3-2022
Date of Completion	17-3-2022
No of Beneficiaries	500



Name of the work with Location	Providing and laying of 2.5 open graded premix carpet on various internal roads of ward No.13.
Department/Organization	H&UDD
Executing Agency	JMC
Block/District	Jammu
AA Cost (Rs. In Lakhs)	29.7
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	29.5
Date of Start (Month/Year)	30-11-2021
Date of Completion(Month/Year)	11-01-2022
No. of beneficiaries	300



Name of the work with Location	Providing and laying of 2.5 open graded premix carpet on various internal roads of ward No.14.
Department/Organization	H&UDD
Executing Agency	JMC
Block/District	
AA Cost (Rs. In Lakhs)	28.82
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	24.25
Date of Start (Month/Year)	05-11-2021
Date of Completion(Month/Year)	18-12-2021
No. of beneficiaries	350

